



School District No. 59 (Peace River South)

April 30, 2025

Board of Education

RE: Capital Projects Update

Crescent Park Elementary School Expansion Project


Since March 12, 2025 the following have occurred:

- March-April 2025
 - Fort Modular, Force Engineering and SD 59 weekly Teams meeting, various emails and phone calls to finalize the plans and get the building permit package ready for submittal.
- March 17, 2025
 - Fort Modular visited the site.
- March 28, 2025
 - Director of Operations and Facilities Manager met with City planners and approvers to discuss the building permit timeline and process.
- April 14, 2025
 - Building permit application submitted to the City.
- April 28, 2025
 - City confirmed review of the modular portion of the project and expressed no code concerns.
- April 28, 2025
 - Fort Modular has the Crescent Park Modular Addition scheduled to start construction in their factory mid-May 2025.
- April 28, 2025
 - Force Engineering continues the preparation of the civil, foundation, earth works tender.

The project budget is:

Ministry funding	\$5,000,000
Ministry contingency funding	2,500,000
Board Contribution	<u>1,700,000</u>
Total	\$9,200,000

Spent to date: \$ 682,445

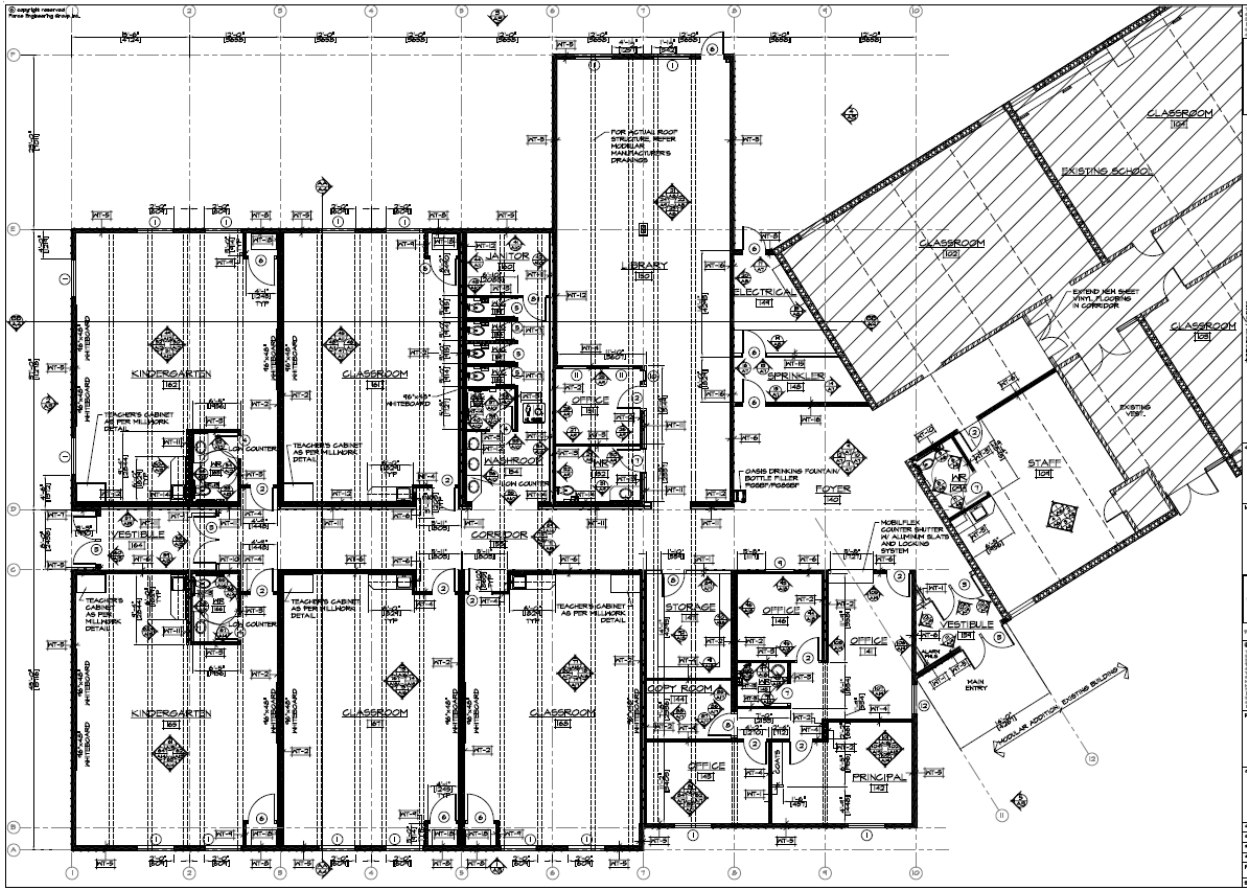

Please follow <https://www.sd59.bc.ca/district/capital-projects> for updates on these projects.

Kim Morris
Secretary-Treasurer/CFO
